



EPiServer

# Ersätt whiteboard med EPiServer Scrum Dashboard för Visual Studio 2010

Pelle Niklasson Development Manager EPiServer

## Historik

- » 2006/7 valde vi att jobba med Microsoft Team Foundation Server
- » Vi ville arbeta med Scrum
- » Vi utvärderade ett flertal Scrum mallar för TFS och valde Conchango (EMC)

# Product backlog


The screenshot shows the Visual Studio Team System Web Access interface. The main content area displays a table of 'All Sprint Backlog Items'. The table has columns for ID, Title, Estimate, Work Re..., State, and Tas. The items listed include tasks like 'Fix R2 breaking changes in UnitTest project', 'EPI Server Lab alme', and 'Implement VPP capabilities configuration'. The interface also includes a search bar, navigation tabs (Home, Work Items, Reports, Documents, Source, Build), and a sidebar with sections for Favorites, New Work Item, My Queries, Team Queries, and Reports.

ID	Title	Estimate...	Work Re...	State	Tas.
14127	Fix R2 breaking changes in UnitTest project	3	2	Deferred	1
10567	EPI Server Lab alme		0	Done	1
12421	Implement VPP capabilities configuration		5	Not Done	1
11471	Sharepoint: WSS VPP- Implement capabilities	8	41	Not Done	
12423	Implement capabilities		20	Not Done	1
11471	Sharepoint: WSS VPP- Implement capabilities	8	41	Not Done	
12424	Documentation		3	Not Done	1
12425	Testing		13	Not Done	1
13918	Tech notes		13	Not Done	1
13919	Installation guide		8	Not Done	1
13920	SDK		3	Not Done	1
14080	User guide			Not Done	1
13361	CMS access in EM SaaS	16	6	In Progress	1
14985	Club-admin crashes if image is missing on disk	4	4	Deferred	1
14986	Author not upmapped to BlogComment	4	0	Done	1
14987	Removed abuse marked topics gives NullReferenceException in report panel	2	0	Done	1
14989	AssignedQuestion.Expert returns null	6	0	Done	1
14983	blnRemoved doesn't have a index.	6	0	Done	1
14984	ClubHandler.GetQueryResult seems to be mapped to get colum 5 instead of 4	10	0	Done	1
15010	Remove Modules-namespace in epicommunity	12	0	Done	1
14993	Traffic Logging: Find issue of 100% cpu	8	0	Done	1
14994	Traffic Logging: Fix issue of 100% cpu	8	0	Done	1

BEHIND EVERY GREAT WEB SITE...

# EPISERVER

# Sprint Backlog, på väggen (Team 1)

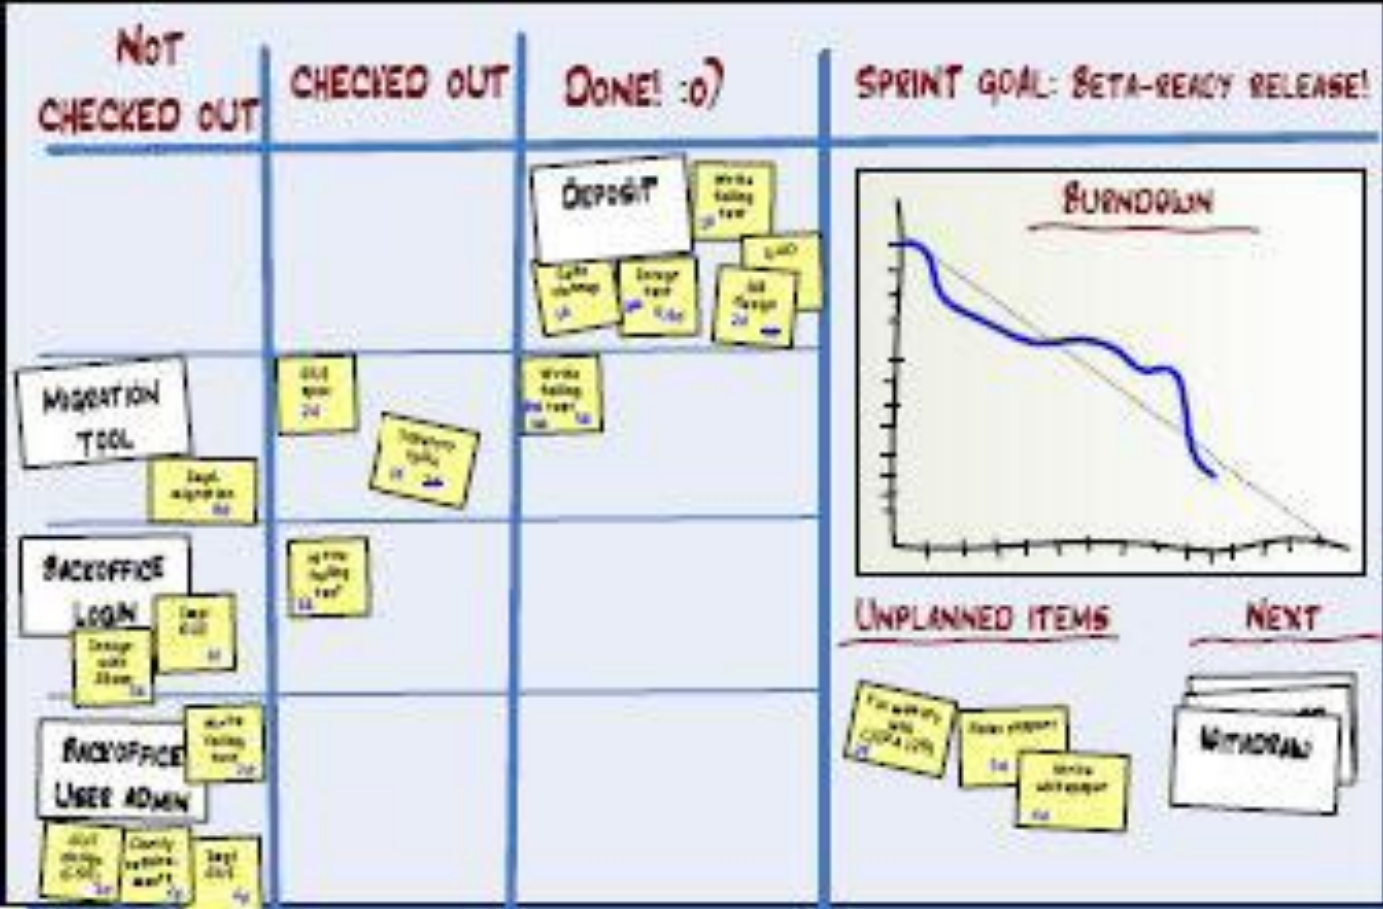

# Sprint Backlog TFS, Team 2

The screenshot displays the Microsoft Team System Web Access interface for a project named 'DevTeamScrum'. The main content area shows the 'All Sprint Backlog Items' table. The table has columns for 'ID', 'Title', 'Estimate...', 'Work Re...', 'State', and 'Tas.'. The items are listed in descending order of estimate.

ID	Title	Estimate...	Work Re...	State	Tas.
14127	Fix R2 breaking changes in UnitTest project	3	2	Deferred	1
10567	EPIServerLab alme		0	Done	1
12421	Implement VPP capabilities configuration		5	Not Done	1
11471	Sharepoint: WSS VPP- Implement capabilities	8	41	Not Done	
12423	Implement capabilities		20	Not Done	1
11471	Sharepoint: WSS VPP- Implement capabilities	8	41	Not Done	
12424	Documentation		3	Not Done	1
12425	Testing		13	Not Done	1
13918	Tech notes		13	Not Done	1
13919	Installation guide		8	Not Done	1
13920	SDK		3	Not Done	1
14080	User guide			Not Done	1
13361	CMS access in EM SaaS	16	6	In Progress	1
14986	Club-admin crashes if image is missing on disk	4	4	Deferred	1
14986	Author not upmapped to BlogComment	4	0	Done	1
14987	Removed abuse marked topics gives NullReferenceException in report panel	2	0	Done	1
14989	AssignedQuestion.Expert returns null	6	0	Done	1
14983	binRemoved doesn't have an index.	6	0	Done	1
14984	ClubHandler.GetQueryResult seems to be mapped to get colum 5 instead of 4	10	0	Done	1
15010	Remove Modules-namespace in epicommunity	12	0	Done	1
14993	Traffic Logging: Find issue of 100% cpu	8	0	Done	1
14994	Traffic Logging: Fix issue of 100% cpu	8	0	Done	1

BEHIND EVERY GREAT WEB SITE...

# EPISERVER

## Team 1, som jobbat traditionellt scrum på en vägg

- + Fick hög delaktighet under scrummötet
- + Mycket bra överblick på status
- Fick svårt att hålla reda på vad som var gjort, av vem osv, lappar kom bort eller föll ner.
- Slarvade med uppdatering i TFS då det inte såg vitsen med detta.
- Övriga medarbetare, management, Kiev, Indien. såg ej status i projektet
- Svårt att jobba på distans eller med distribuerade team.


## Team 2, som jobbat direkt i TFS,

- + Behövde inte uppdatera både lappar och i TFS
- + Burndown fungerade direkt
- + All historik finns kvar efter sprinten
  
- Dålig delaktighet på scrummötet
- Dålig överblick när det är en lista.
- Övriga medarbetare, management, Kiev, Indien.  
Hade svårt att förstå status.

## Utmaningar

- » Öka delaktigheten i teamet
- » Dra nytta av systemstöd
- » Skapa insyn i projektet
- » Stödja scrum i en globalorganisation

# EPiServer Scrum dashboard for TFS 2008

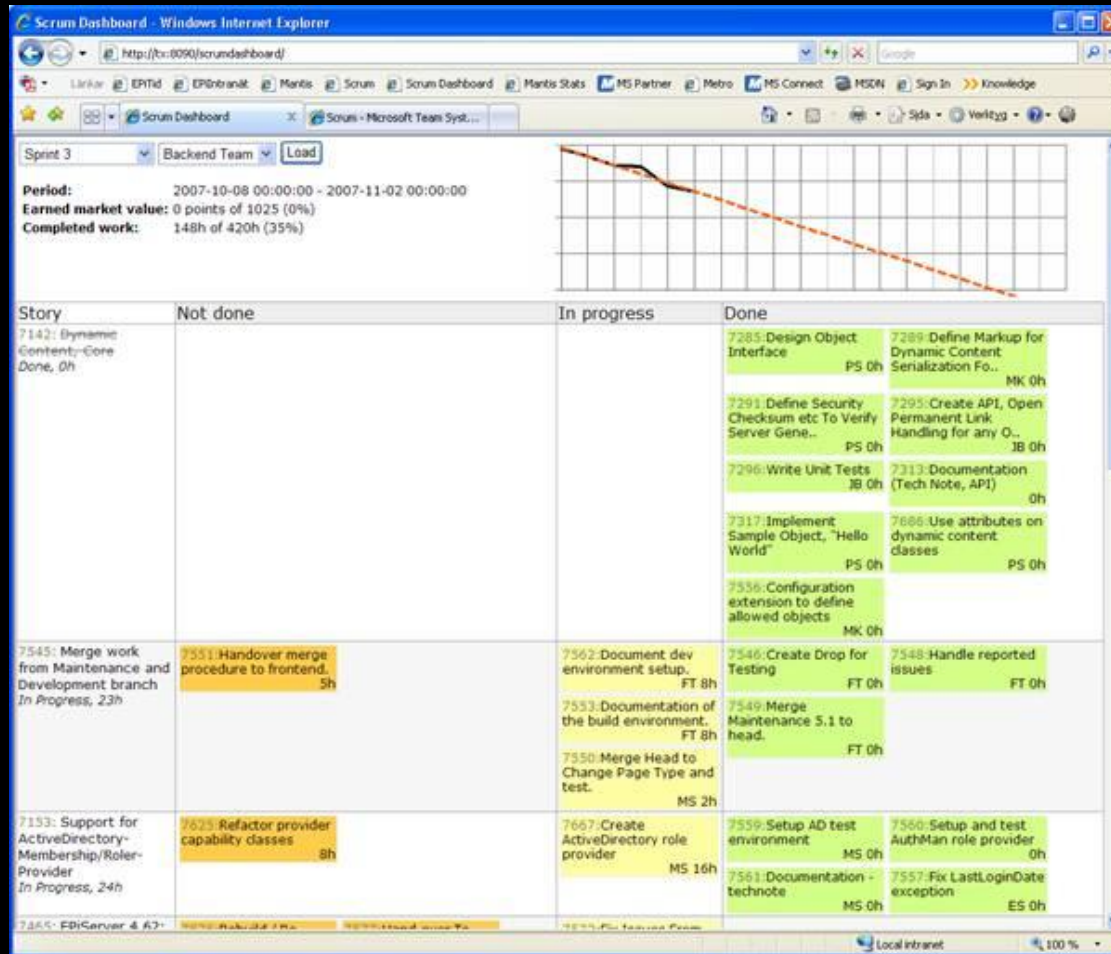

BEHIND EVERY GREAT WEB SITE...

**EPISERVER**

# Editera en Task

The screenshot displays a web application interface for managing a sprint. At the top, there's a navigation bar with various links. Below it, a dashboard shows the current sprint: "Sprint 2" for the "Backend Team". The period is from 2007-10-08 00:00:00 to 2007-11-02 00:00:00. The earned market value is 0 points of 1025 (0%), and completed work is 148h of 420h (35%).

The main area shows a sprint backlog table with columns for story ID, story description, and task details. A task editor window is open over the table, showing details for "Sprint Backlog Item #7551: Handover merge procedure to frontend".

Story	Not done
7142: Dynamic Content-Elem Done, 0h	
7545: Merge work from Maintenance and Development branch. In Progress, 23h	7551: Handover merge procedure to frontend. 5h
7153: Support for ActiveDirectory-Membership/Role-Provider. In Progress, 24h	7635: Refactor provider capability classes. 8h
7485: EPIServer 4.62; Release. In Progress, 10h	7570: Rebuild / Re-release. 1h
7420: Migration; Raw	7560: Migrate database. 7560: Migrate files.

The task editor window for item #7551 shows the following fields:

- Title: Handover merge procedure to frontend.
- Planning: Sprint Number (3), Area (Scrum), Estimated Effort (5), Work Remaining (3).
- Status: Backlog Item Type (Task), Owned By, Current Status (Not Done).
- Description: (Empty text area)

10

## TFS 2010

- » När TFS 2010 kom så valde Conchango nu mera EMC att bygga en helt nya Scrum implementation för TFS.
- » Vilket ledde till att vi också valde att bygga en ny scrum dashboard baserad på dessa mallar.

# EPiServer Scrum dashboard for TFS 2008

Home Options About

## TestingScrum3RC

Id	Title	State	Start	End
#41018	Release 01\3 week sprints\Sprint 14	Not Started	2010-12-23	2011-01-12
#41016	Release 01\3 week sprints\Sprint 13	Not Started	2010-12-02	2010-12-22
#41014	Release 01\3 week sprints\Sprint 12	Not Started	2010-11-11	2010-12-01
#41012	Release 01\3 week sprints\Sprint 11	Not Started	2010-10-21	2010-11-10
#41010	Release 01\3 week sprints\Sprint 10	Not Started	2010-09-30	2010-10-20
#41008	Release 01\3 week sprints\Sprint 09	Not Started	2010-09-09	2010-09-29
#41006	Release 01\3 week sprints\Sprint 08	Not Started	2010-08-19	2010-09-08
#41004	Release 01\3 week sprints\Sprint 07	Not Started	2010-07-29	2010-08-18
#41002	Release 01\3 week sprints\Sprint 06	Not Started	2010-07-08	2010-07-28
#41000	Release 01\3 week sprints\Sprint 05	Not Started	2010-06-17	2010-07-07
#40998	Release 01\3 week sprints\Sprint 04	Not Started	2010-05-27	2010-06-16
#40996	Release 01\3 week sprints\Sprint 03	Not Started	2010-05-06	2010-05-26
#40994	Release 01\3 week sprints\Sprint 02	Not Started	2010-04-15	2010-05-05
#40992	Release 01\3 week sprints\Sprint 01	Not Started	2010-03-25	2010-04-14

#40992	Release 01\3 week sprints\Sprint 01	Not Started	2010-03-25	2010-04-14
#40994	Release 01\3 week sprints\Sprint 02	Not Started	2010-04-15	2010-05-05
#40996	Release 01\3 week sprints\Sprint 03	Not Started	2010-05-06	2010-05-26
#40998	Release 01\3 week sprints\Sprint 04	Not Started	2010-05-27	2010-06-16
#41000	Release 01\3 week sprints\Sprint 05	Not Started	2010-06-17	2010-07-07
#41002	Release 01\3 week sprints\Sprint 06	Not Started	2010-07-08	2010-07-28
#41004	Release 01\3 week sprints\Sprint 07	Not Started	2010-07-29	2010-08-18
#41006	Release 01\3 week sprints\Sprint 08	Not Started	2010-08-19	2010-09-08
#41008	Release 01\3 week sprints\Sprint 09	Not Started	2010-09-09	2010-09-29
#41010	Release 01\3 week sprints\Sprint 10	Not Started	2010-09-30	2010-10-20
#41012	Release 01\3 week sprints\Sprint 11	Not Started	2010-10-21	2010-11-10
#41014	Release 01\3 week sprints\Sprint 12	Not Started	2010-11-11	2010-12-01
#41016	Release 01\3 week sprints\Sprint 13	Not Started	2010-12-02	2010-12-22
#41018	Release 01\3 week sprints\Sprint 14	Not Started	2010-12-23	2011-01-12

BEHIND EVERY GREAT WEB SITE...

EPISERVER

# EPiServer Scrum dashboard for TFS 2008

http://tfs01vm:8080/Scrum/Dashboard?project=TestingScrum3RC&sprint=40992

Project: TestingScrum3RC Sprints: Release 0113 week sprints\Sprint 01 Teams: <all> Load

Logged in as Pelle Niklasson

Overview  Tasks  Acceptance tests  Impediments  Assigned to me  Expand all

New.. Add..

**Do this (#41024) In Progress** In Progress, 5 story points, 8h remaining

**Tasks** Add.. Import..

Not Started					In Progress	Done
#41785 test 0h	#41985 Mir: The Status message on Mirroring Service in some case is mismatch between 0h	#41989 test 0h	#41990 test 0h	#41991 test 0h	#41025 Work 1 8h	
#41992 test 0h	#41993 test 0h	#41994 test2 0h	#41995 test 0h	#41996 test2 0h	#41786 test2 0h	
#42003 test 0h	#42004 test 0h	#44125 New item 2 2h	#44127 My new Item 2h		#41791 sdsdsd 0h	

**Acceptance tests** Add.. Import..

Not Implemented	Ready For Test		Failed	Passed
	#44093 test	#44094 test2		#41792 Accept this

BEHIND EVERY GREAT WEB SITE...

**EPiSERVER**

## Demo

- » **EPiServer Scrum Dashboard for Microsoft Team Foundation Server 2010 Demo**
- » [www.youtube.com/watch?v=UWejn-qRMJ0](http://www.youtube.com/watch?v=UWejn-qRMJ0)

# scrumdashboard.codeplex.com

Scrum Dashboard - Windows Internet Explorer

http://scrumdashboard.codeplex.com/

CodePlex Open Source Community

Register | Sign In | CodePlex Home

Search all CodePlex projects Search

Home Downloads Documentation Discussions Issue Tracker Source Code People License

View All Comments | Print View | Page info | Change History (all pages) Search Wiki & Documentation

### Project Description

Scrum Dashboard is a web front-end for Scrum for Team System from EMC2 (formerly known as Conchango). The main goal of this project is to replace the whiteboard and simplify daily work with Scrum artifacts in Team Foundation Server.

### Features

- Ajax-based web interface with support for Internet Explorer and Firefox
- All features are sprint-centric for daily work in a sprint
- Create, add and update product backlogs
- Create and update sprint backlog items (task, impediment, bug)
- Drag and drop of sprint backlog items between states
- Inline editing of work remaining as you go
- Colorized sprint backlog items to visually see progress and unplanned work
- Import bugs for maintenance tasks (even from another project in TFS)
- Statistics and sprint burndown chart easily visible for the team
- RSS feed for syndication of changes in product backlog
- Automatically displays new projects, sprints and teams from TFS without configuration

### Activity

7 30 All days

Page Views	1478
Visits	420
Downloads	109

View Detailed Stats

### EPISERVER SCRUM DASHBOARD

Project: Testing project for Scrum 2.0  
Sprint: Release T1 Sprint 2  
Team: Backend Team

Period: 2008-05-19 - 2008-05-26  
Current effort: 8 of 30 (26%)  
Completed work: 12h of 63h (18%)

36 h Not Done  
x 3 In Progress  
x 0 Ready for Test  
12 h Done  
4 h Not Planned

Product Backlog	Not Done	In Progress	Ready for Test	Done
10472: A new feature In Progress, 10 points, 20h #10474 Deliver to test	#10476 Refactor	#10475 AS, 8h	#10478 Do nothing	#10479 CK, 8h #10522 AL, 8h

BEHIND EVERY GREAT WEB SITE...

# EPISERVER

## Ni hittar

Conchango

[www.scrumforteamssystem.com](http://www.scrumforteamssystem.com)

EPiServer ScrumDashboard

[scrumdashboard.codeplex.com](http://scrumdashboard.codeplex.com)

» **Downloads: 99062**

**Pelle Niklasson**  
**EPiServer AB**  
Regeringsgatan 67  
Stockholm  
Sweden

Tel: +46 (0)8 555 827 33  
Pelle.niklasson@episerver.com
